

MONTVIEW BOULEVARD PRESBYTERIAN CHURCH


WEEKLY UPDATE

Week of **November 12, 2020**

1. Painting in the Sanctuary is complete. The Narthex and touch up paint will be finished before November 23.
2. Colarelli Construction has obtained the nonstructural demo permit. This allows demolition work of doors, casework (to be salvaged), and carpet to start prior to receipt of building permit. We expect to start selective demolition work the week of December 14.
3. Colarelli Construction will be installing secure, temporary partitions the week of December 7. This will contain construction work to immediate area. An access plan of these areas is attached.
4. The elevator is complete. New flooring samples have been ordered for review and door component has been fixed. Elevator will not be used during construction.

Upcoming: Bids will be received by Colarelli on November 24 and we will start our internal review of scopes and pricing. We expect to have pricing compiled and ready for review by the Building Committee on December 7.



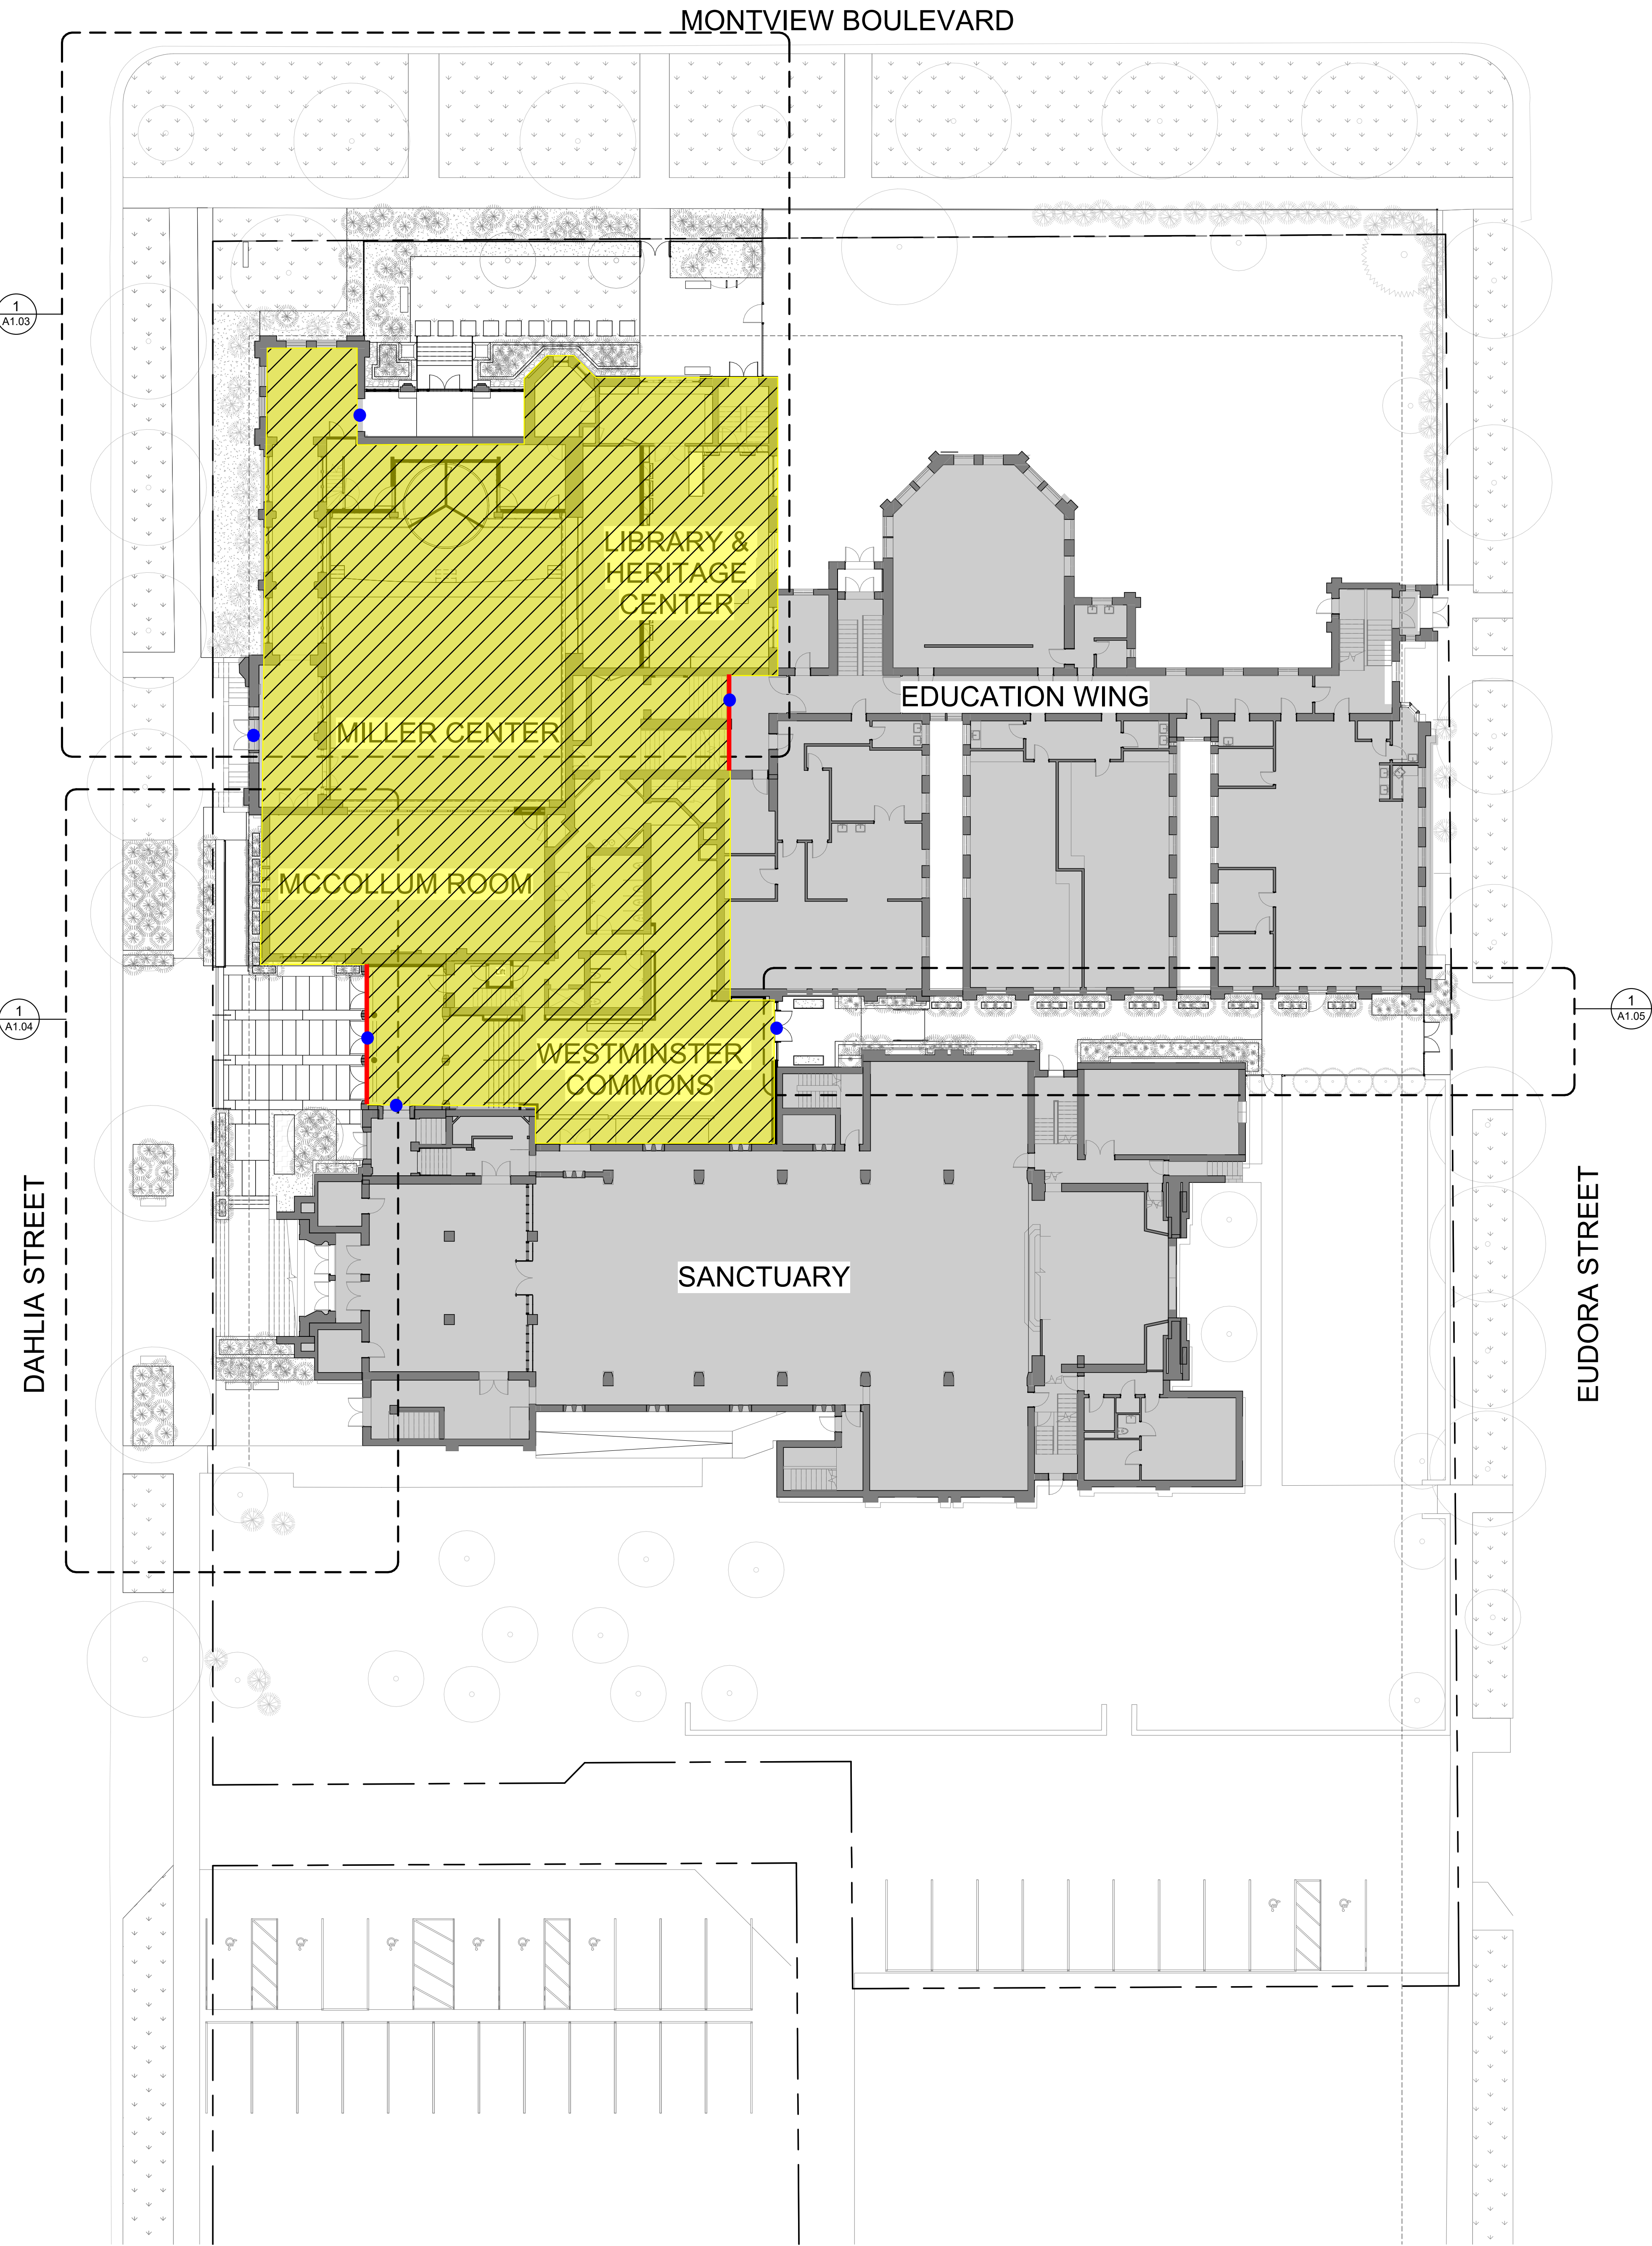

- ▨ CONTRACTOR ACCESS
- PARTITION WALL
- SECURED DOOR

- SITE PLAN GENERAL NOTES**
1. ALL EXISTING TREES AND PLANTINGS TO REMAIN UNLESS OTHERWISE NOTED, CONTRACTOR TO PROTECT DURING CONSTRUCTION.
 2. ALL EXISTING SIDEWALKS AND PLAZA TO REMAIN UNLESS OTHERWISE NOTED, CONTRACTOR TO PROTECT DURING CONSTRUCTION.
 3. SEE CIVIL AND LANDSCAPE DRAWINGS FOR ADDITIONAL INFORMATION.

LEGEND

<ul style="list-style-type: none"> EXISTING BUILDING ELEMENT TO REMAIN EXISTING BUILDING ELEMENT TO BE DEMOLISHED/REMOVED - SEE ADDITIONAL NOTES IN KEYNOTES AND GENERAL NOTES EXISTING FLOOR AREA TO BE DEMOLISHED/REMOVED 	<ul style="list-style-type: none"> NEW BUILDING ELEMENT (SEE A7.01 FOR PARTITION TYPE) NEW FLOOR AREA AREA WITH NO WORK
<ul style="list-style-type: none"> PROPERTY LINE BUILDING SETBACK SCOPE OF WORK 	

MONTVIEW CHURCH
1980 DAHLIA STREET
DENVER, COLORADO 80220

TRYBA ARCHITECTS
1620 Logan Street
Denver, Colorado 80203
303.831.4010

STAMP:

NOT FOR CONSTRUCTION
PROGRESS SET ONLY

ISSUE		
NO.	DATE	DESCRIPTION
04.02.2020	100% SCHEMATIC DESIGN	
06.11.2020	100% DESIGN DEVELOPMENT	

<p style="margin: 0;">PROJECT NO. 1902</p> <p style="margin: 0;">DATE: JUNE 11, 2020</p>	<p style="margin: 0;">MONTVIEW CHURCH</p>
<p style="margin: 0;">A1.02</p>	
<p style="margin: 0;">DRAWING TITLE: SITE PLAN - PROPOSED</p>	

06/11/2020 5:13:21 PM
